Programme summary


PROJECT Coombe Lane

SITE Coombe Lane
Westhay Green
Anytown
BZ23 4CD

DATE 9 November 2026

STATUS Working copy: last issued as Rev A

Task	Days	Start	Finish
Land, finance and insurance	15	6 Dec 24	14 Jan 25
Design team appointment	20	6 Dec 24	21 Jan 25
Design to submission	65	22 Jan 25	24 Apr 25
Surveys and investigation	15	22 Jan 25	11 Feb 25
Planning	116	15 Apr 25	30 Sep 25
Building control and warranty	60	29 Jul 25	21 Oct 25
Permits and licences	100	16 Apr 25	9 Sep 25
Procurement	160	25 Apr 25	9 Dec 25
Health, safety and CDM	212	8 Oct 25	21 Aug 26
Technical design and construction issue	60	29 Jul 25	21 Oct 25
Start on site		3 Nov 25	
Site start and establishment	5	3 Nov 25	7 Nov 25
Groundworks to Stage 1	28	10 Nov 25	17 Dec 25
Superstructure: DPC to wall plate	29	12 Dec 25	6 Feb 26
Roof and watertight	10	9 Feb 26	20 Feb 26
First fix	19	23 Feb 26	19 Mar 26
Close up	35	20 Mar 26	12 May 26
Second fix	21	13 May 26	11 Jun 26
Finishes and third fix	23	12 Jun 26	14 Jul 26
Scaffold strike	4	23 Feb 26	26 Feb 26
Service connections	70	4 Nov 25	25 Feb 26
External works	6	15 Jul 26	22 Jul 26
Snagging and commissioning	19	15 Jul 26	10 Aug 26
Handover and completion	9	11 Aug 26	21 Aug 26

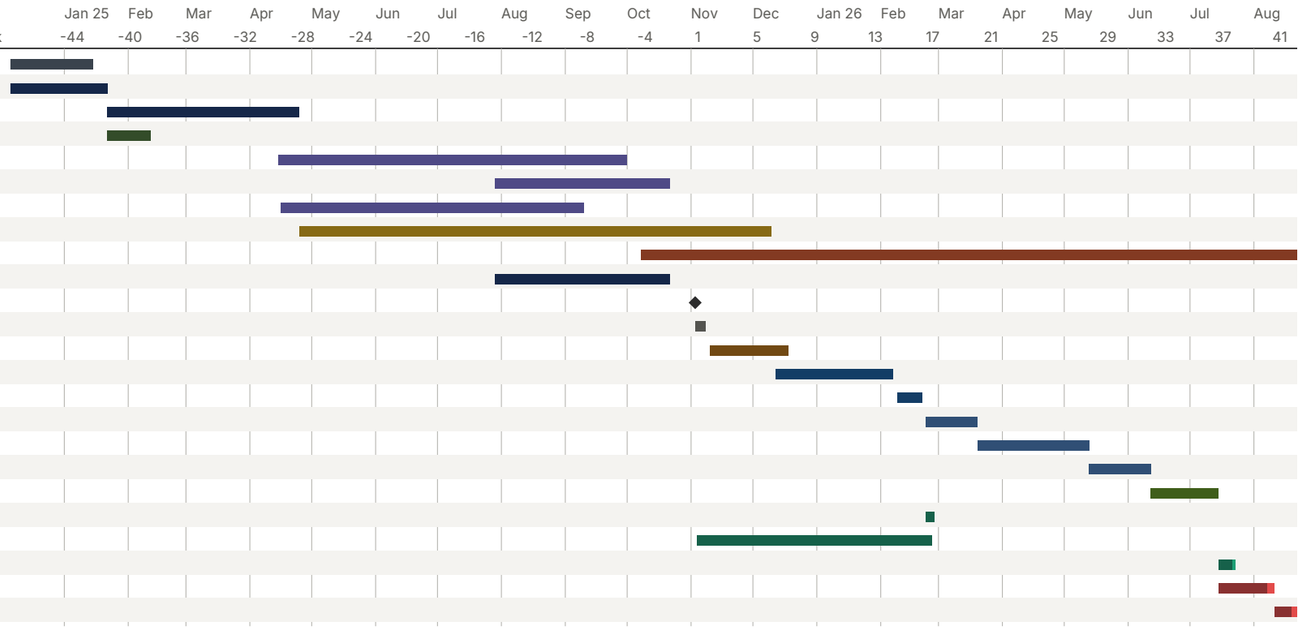

This record was assembled by its owner using The Modern Housebuilder. Its contents have not been checked or verified by The Modern Housebuilder.
This document contains the material its owner chose to include. It is not necessarily their complete record.
