
Programme summary

PROJECT Ings Lane
SITE Ings Lane
Thornby Moor
Anytown
BZ24 6EF
DATE 9 November 2026
STATUS Working copy: last issued as Rev A

Task	Days	Start	Finish
Land, finance and insurance	16	29 Sep 25	20 Oct 25
Design team appointment	21	29 Sep 25	27 Oct 25
Design to submission	53	28 Oct 25	26 Jan 26
Surveys and investigation	15	28 Oct 25	17 Nov 25
Planning	128	19 Jan 26	21 Jul 26
Building control and warranty	63	14 May 26	11 Aug 26
Permits and licences	111	20 Jan 26	29 Jun 26
Procurement	246	26 Sep 25	29 Sep 26
Health, safety and CDM	379	18 Nov 25	15 Jun 27
Technical design and construction issue	63	14 May 26	11 Aug 26
Start on site		24 Aug 26	
Site start and establishment	5	24 Aug 26	28 Aug 26
Groundworks to Stage 1	37	1 Sep 26	21 Oct 26
Superstructure: DPC to wall plate	21	15 Oct 26	12 Nov 26
Roof and watertight	12	13 Nov 26	30 Nov 26
External face	41	1 Dec 26	10 Feb 27
First fix	19	1 Dec 26	11 Jan 27
Close up	35	12 Jan 27	1 Mar 27
Second fix	21	2 Mar 27	1 Apr 27
Finishes and third fix	23	2 Apr 27	5 May 27
Scaffold strike	4	11 Feb 27	16 Feb 27
Service connections	31	22 Oct 26	3 Dec 26
External works	16	6 May 27	27 May 27
Snagging and commissioning	19	6 May 27	2 Jun 27
Handover and completion	9	3 Jun 27	15 Jun 27

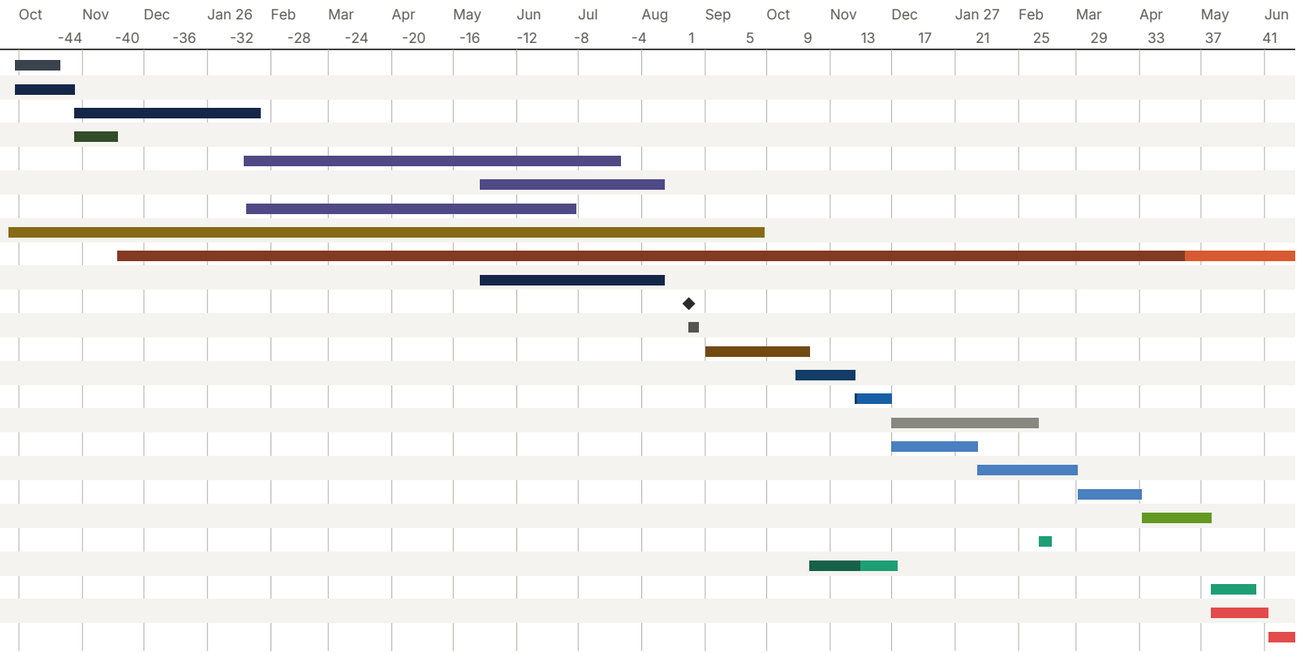

This record was assembled by its owner using The Modern Housebuilder. Its contents have not been checked or verified by The Modern Housebuilder.
This document contains the material its owner chose to include. It is not necessarily their complete record.
